

PHOTO REPORT

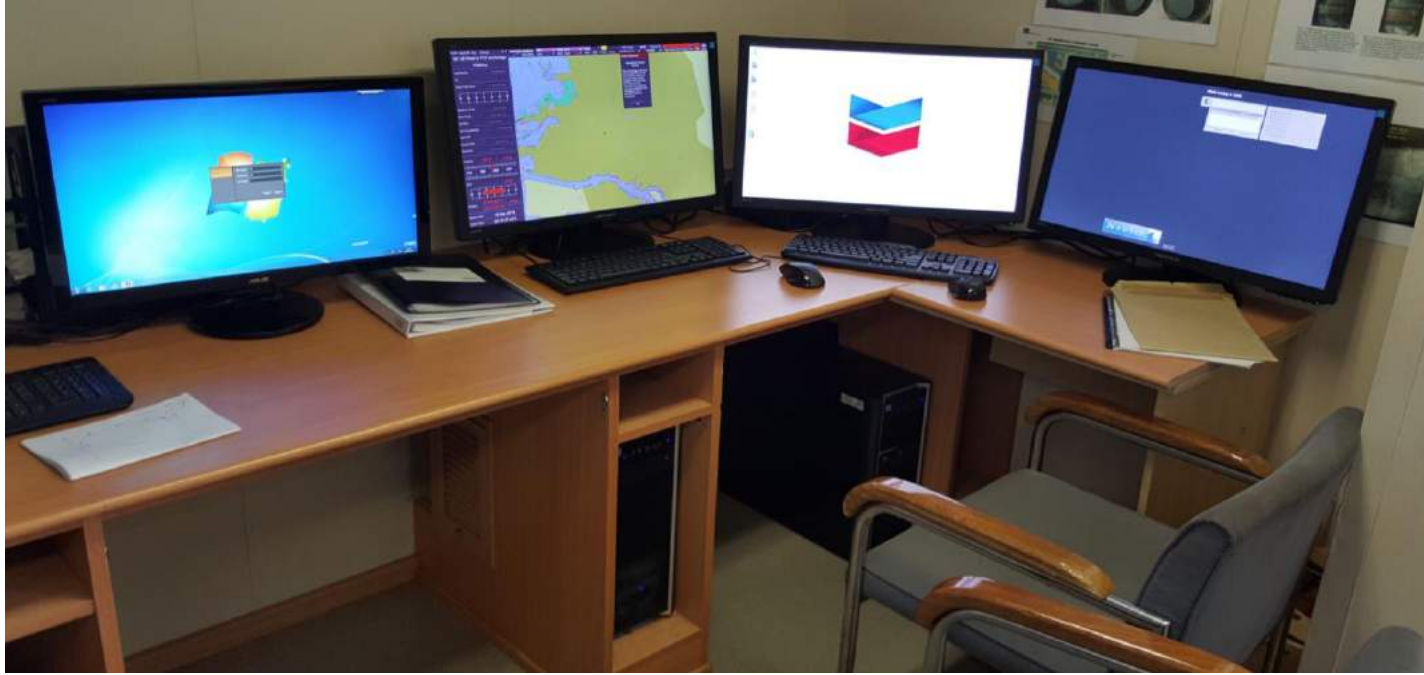

Messr.

Job No. : 2623

Date : 29th April 2016

Location : Singapore Anchorage

Pg1

No.	Description
<p>Subject : Replacement of Computer Desk for Simulators Location: C-Deck Training Room Table Dimension: L4000 + 1590mm + 1360mm x W700 + 580mm x H760mm</p>	
	
<p align="center">Existing Computer Desk for Simulators in C-Deck Training room</p>	

No.	Description
-----	-------------










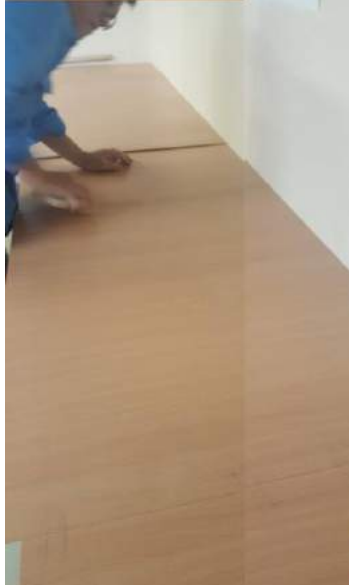
Ship Crew started dismantling and removing computer simulators from existing table upon arrival.









Carpentry Team carried out surface preparation, for installing new tables while simulators were being removed

No.	Description
	
	
	
<p style="text-align: center;">Existing table was dismantled into parts</p>	

No.	Description
	 <p>> All parts of the dismantled table were placed outside the training room and handed over to ship crew for disposal</p> <p>> Housekeeping was done in the area before commencing works for installation of new table</p>
	 <p>New Table frames were fitted into place, and checked for any obstructions, before being secured firmly into position</p>
	 <p>Manual holes were cut out on supporting leg frames to cater to running cables and plugs</p>

No.	Description
	 
<p>Top part of the table was fitted into place, obstruction at the edge was found, and adjustment was done and refitted</p>	
	
<p>After Table top arced sides were installed. Centre top part was adjusted and fitted into position</p>	
	 
<p>Top finishing layer of Table top was cut, glued, and secured accordingly</p>	

No.	Description
	
<p>Table edge pieces were cut accordingly and fitted into position. Chamfering was done to smoothen surface & edges</p>	
	
<p>Three manual holes were cut out on table top to cater to running cables and plugs</p>	

No.	Description
	

- > Premium Wood Fillers were applied to fill the gaps
- > Total of two Coat Varnish was applied on wooden edges one after the other with curing time in between



- > Final Touch up was done: Silicon on wall edges, thorough surface cleaning of table, Housekeeping of area.

No.	Description
-----	-------------



> Final condition of table was inspected by Chief Engineer and found Satisfactory
